

- LEGEND**
- PROPOSED DETOUR ROUTE (APPROXIMATELY 3.1 MILES)
 - ▨ MAJOR PIPE REPLACEMENT LOCATION
 - ▾ TEMPORARY TYPE B SIGN POST
 - TT TEMPORARY TYPE III BARRICADE
 - ① SIGN NUMBER
 - INTERSTATE
 - STATE ROAD
 - TOWNSHIP ROAD
 - - - MUNICIPAL BOUNDARY

WEEKEND DETOUR FOR MAJOR PIPE REPLACEMENTS

- TRAFFIC WILL BE MAINTAINED USING DAILY FLAGGING OPERATIONS DURING THE MAJORITY OF CONSTRUCTION ACTIVITIES SUCH AS WIDENING, PAVING, MINOR DRAINAGE PIPE REPLACEMENTS, GUIDE RAIL INSTALLATION AND VEGETATION REMOVAL.
- TWO BRIDGE REPLACEMENTS WITHIN THE CORRIDOR WILL OCCUR USING ALTERNATING BI-DIRECTIONAL STAGED CONSTRUCTION CONTROLLED WITH TEMPORARY TRAFFIC SIGNALS. REFER TO THE BRIDGE LOCATIONS IDENTIFIED ABOVE WITH DETAILS ON THE RIGHT OF THIS SHEET. BOTH BRIDGE REPLACEMENTS ARE ANTICIPATED TO BE BUILT AT THE SAME TIME.
- SEVERAL MAJOR CROSS PIPE REPLACEMENTS (SIZES 36" DIAMETER OR GREATER) WILL REQUIRE SHORT-TERM WEEKEND CLOSURES OF CAMP BETTY WASHINGTON ROAD WITH THE PIPE LOCATIONS AND DETOUR ROUTE PROVIDED ABOVE.
- ACCESS TO PARCELS WITHIN THE CORRIDOR WILL BE MAINTAINED DURING CONSTRUCTION.
- TRAFFIC CONTROL COORDINATION WITH KEY STAKEHOLDERS SUCH AS EMERGENCY SERVICE PROVIDERS, SCHOOL DISTRICTS, ETC., WILL OCCUR DURING BOTH DESIGN AND CONSTRUCTION PHASES.
- KEY CHANGES TO TRAFFIC CONTROL DURING CONSTRUCTION WILL BE COMMUNICATED TO MOTORISTS IN ADVANCE USING SIGNING, MESSAGE BOARDS, MEDIA AND BY OTHER MEANS.


DETOUR SIGN TABULATION

INCLUDED IN LUMP SUM ITEM 0901-0001 (FOR INFORMATION ONLY)


SIGN GROUP NO.	DEPICTION	SERIES	SIZE	MOUNTING	QTY	FLASHER
1	ROAD CLOSED	R11-2	48"x30"	TYPE III BARRICADE	4	2 TYPE B
2	ROAD CLOSED TO THRU TRAFFIC (DETOUR)	R11-4 M4-10R	60"x30" 48"x18"	TYPE III BARRICADE	2	2 TYPE B
3	ROAD CLOSED 1/2 MILES AHEAD LOCAL TRAFFIC ONLY (DETOUR)	R11-3A M4-10L SP-1	60"x30" 48"x18" 54"x18"	TYPE III BARRICADE	2	2 TYPE B
4	ROAD CLOSED 500 FT	W20-3 W30-1-1	36"x36" 20"x6"	TYPE III BARRICADE	2	1 TYPE B
5	ROAD CLOSED 1000 FT	W20-3 W30-1-2	36"x36" 20"x6"	TYPE III BARRICADE	2	1 TYPE B
6	CAMP BETTY WASHINGTON RD DETOUR 1/2 MILE	SP-1 W20-2 W30-1-4	54"x18" 36"x36" 20"x6"	TYPE III BARRICADE	2	1 TYPE B
7	CAMP BETTY WASHINGTON RD DETOUR 1500 FT	SP-1 W20-2 W30-1-3	54"x18" 36"x36" 20"x6"	TYPE III BARRICADE	2	1 TYPE B
8	CAMP BETTY WASHINGTON RD DETOUR AHEAD	SP-1 W20-2 W30-1-6	54"x18" 36"x36" 20"x6"	TYPE III BARRICADE	2	1 TYPE B
9	CAMP BETTY WASHINGTON RD DETOUR	SP-1 M4-9SL	54"x18" 30"x24"	TYPE B POST	6	
10	CAMP BETTY WASHINGTON RD DETOUR	SP-1 M4-9L	54"x18" 30"x24"	TYPE B POST	6	
11	CAMP BETTY WASHINGTON RD DETOUR	SP-1 M4-9SR	54"x18" 30"x24"	TYPE B POST	7	
12	CAMP BETTY WASHINGTON RD DETOUR	SP-1 M4-9R	54"x18" 30"x24"	TYPE B POST	7	
13	CAMP BETTY WASHINGTON RD DETOUR	SP-1 M4-9S	54"x18" 30"x24"	TYPE B POST	9	
14	CAMP BETTY WASHINGTON RD END DETOUR	SP-1 M4-8A	54"x18" 24"x18"	TYPE B POST	2	
15	CMS	CMS			2	

* INSTALL SIGNS 9 AND 10 OR 11 AND AS APPROPRIATE ON SIDE ROADS APPROACHING CAMP BETTY WASHINGTON ROAD, BASED ON WHICH WEEKEND CLOSURE IS ACTIVE

BRIDGE REPLACEMENT OVER MILL CREEK

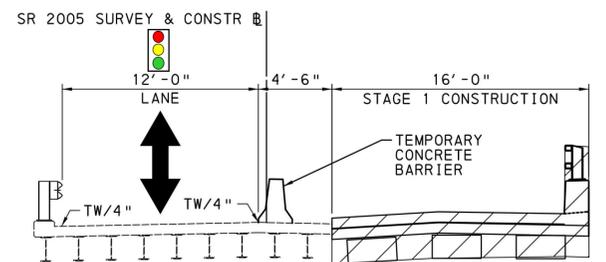


STAGE 1 CONSTRUCTION SR 2005 OVER MILL CREEK

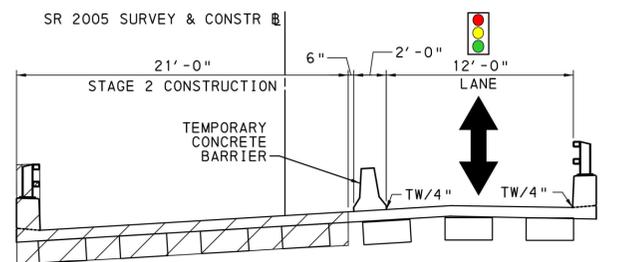


STAGE 2 CONSTRUCTION SR 2005 OVER MILL CREEK

BRIDGE REPLACEMENT OVER TRIBUTARY TO MILL CREEK

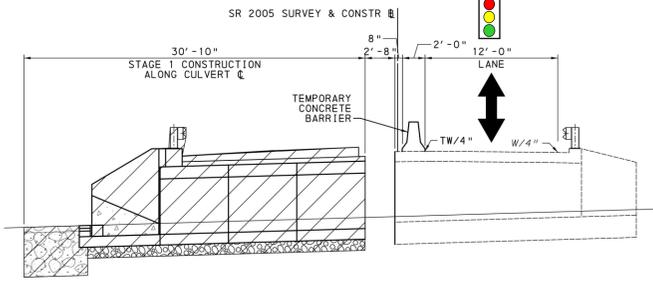

STAGE 1 CONSTRUCTION SR 2005 OVER TRIBUTARY TO MILL CREEK

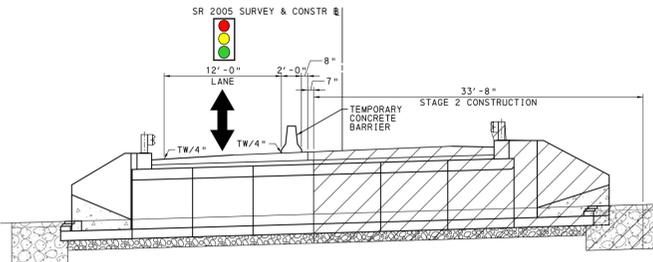

STAGE 2 CONSTRUCTION SR 2005 OVER TRIBUTARY TO MILL CREEK



SR 2005-004 - PAVEMENT WIDENING, OVERLAY, BRIDGE REPLACEMENTS AND SAFETY IMPROVEMENT PROJECT
YORK & SPRINGGETTSBURY TOWNSHIPS, YORK COUNTY

